



[Subject]

Village of Marengo Sanitary Sewer Improvements Weekly Construction Update 2/16/2026

[Keywords]

Overall Project Status

Currently both bores across SR 229 are complete and the SR 229 pump station has been set. Approximately 700' of 12" sanitary and manholes #16 - #18 and manhole #20 have been installed. To date, 115' of 12" and manhole #19 remain (and 3 ea. 6" laterals) to complete section along SR 229.

Progress last week

Last week the contractor began at MH #17 and finished the week 120' down station of MH #19. Winkler Excavating was on site , completing directional drilling of the 4" force main from the treatment plant to the east side of proposed Walnut St. Pump Station.

Planned Activities This Week

This week Dirt Dawg will finish the 12" along SR 229 then begin work on the Walnut St. Pump Station. NCI is scheduled to be on site this week to set the pump station.


Ongoing Items that Need Addressed

Electric for 229 Pump Station

K.E. McCartney & Associates, Inc.

February 16, 2026

Recent Photos

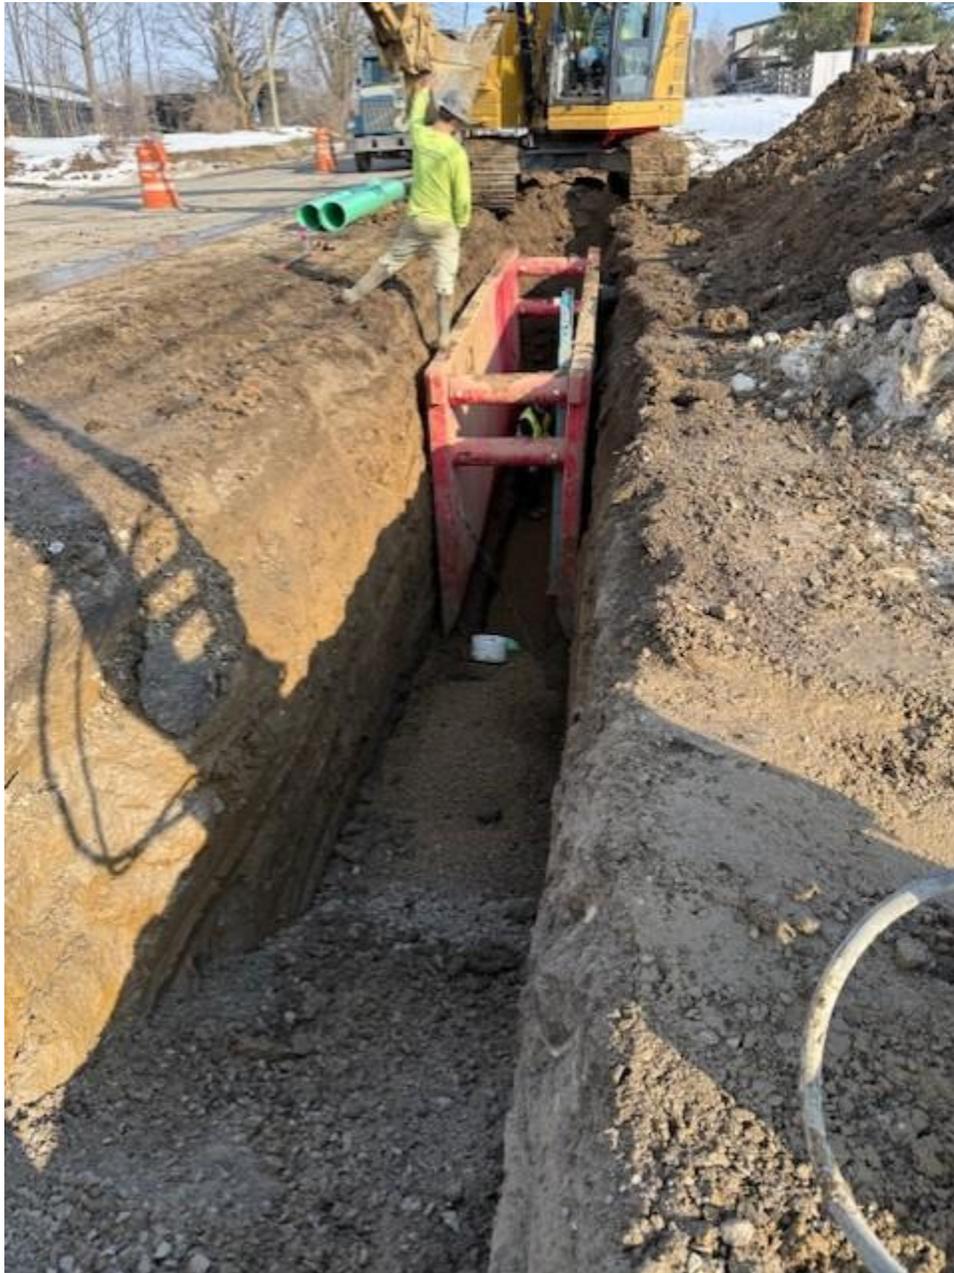

Recent Photos



K.E. McCartney & Associates, Inc.

February 16, 2026

Recent Photos

