



Village of Marengo Sanitary Sewer Improvements

Weekly Update 3-2-26

Overall Project Status

Currently all the sanitary along SR 229 has been put in place and the contractor has begun installing 12" pipe out of the Walnut St. pump station toward Main Street.

Progress last week

Last week the contractor finished the 6" laterals on the south side of 229. They tied in the remaining 85' of 4" force main from the treatment plant, connecting the line to the Walnut St. pump station. They then began installing 12" west from Walnut St. pump station, set drop MH #8 and ended the week 75' downstream of MH #7.

Planned Activities This Week

This week Dirt Dawg will continue installing 12" along the south side of Walnut Street toward Main Street. They will also be replacing the 10" storm line that is in conflict with the 12" sanitary.

Ongoing Items that Need Addressed

Estimated timeline and cost for electric service to pump stations.

Recent Photos


Sewer tie-in at new house on SR. 229



K.E. McCartney & Associates, Inc.
- Weekly Update 3-2-26
March 2, 2026

Recent Photos

4 inch force main

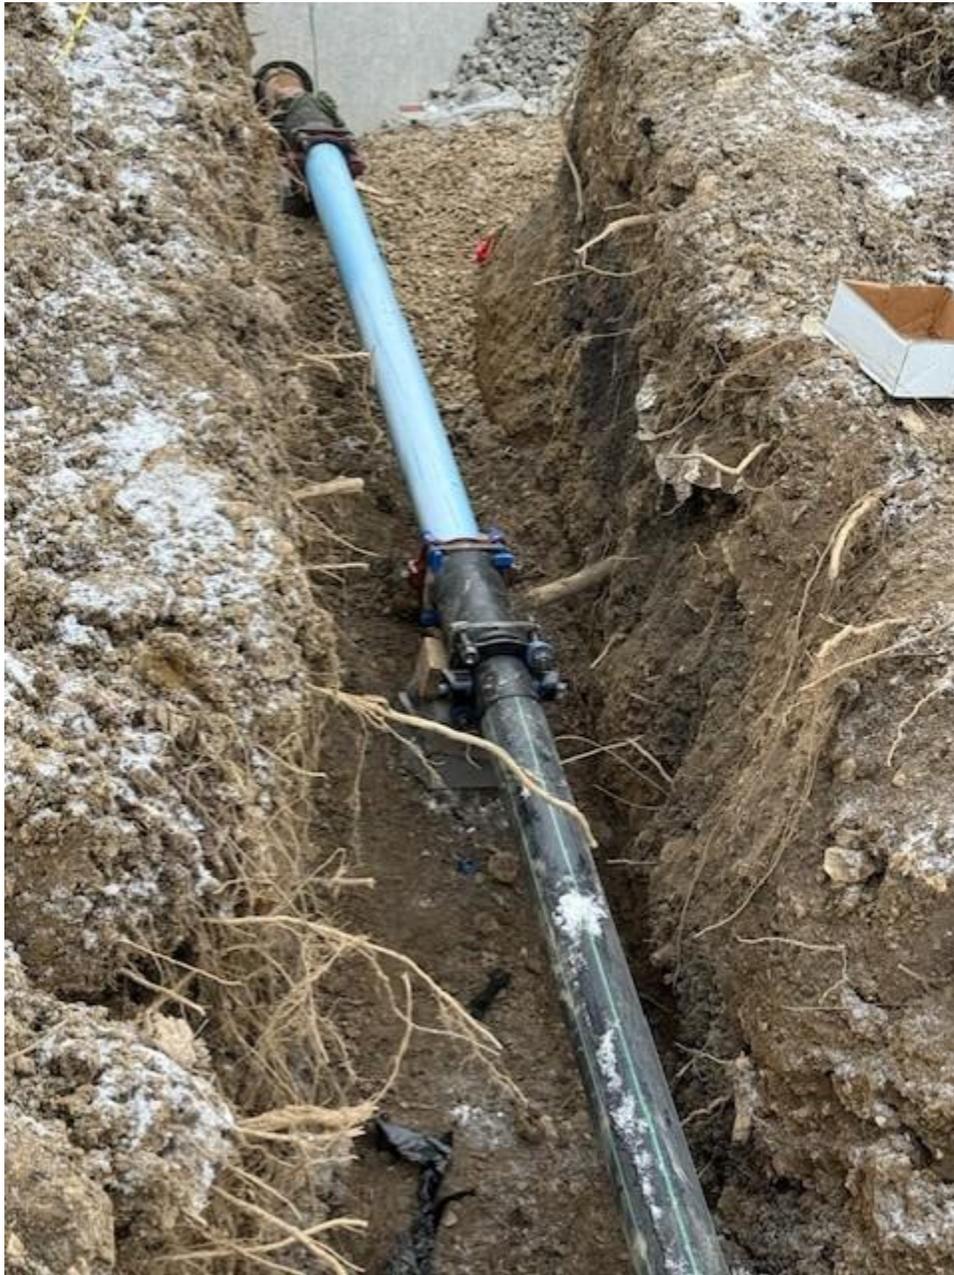

Recent Photos
Manhole #8

